


Network solution

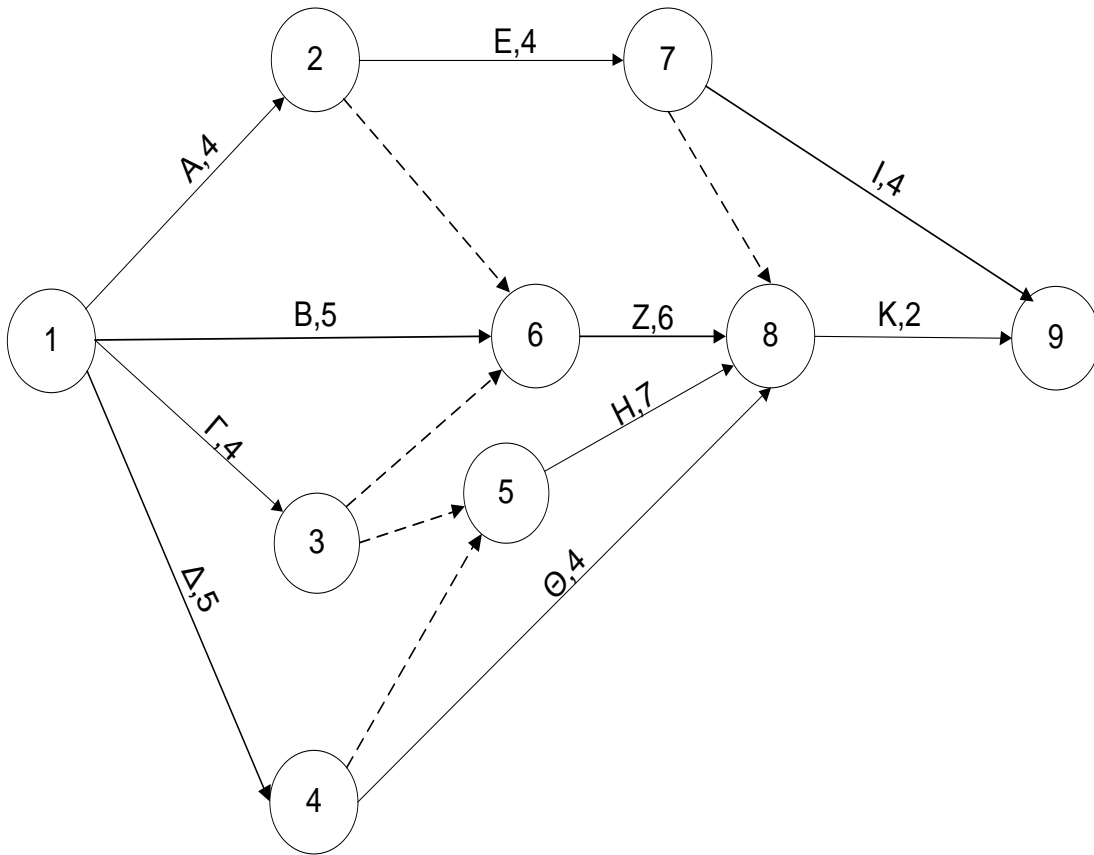

Results

Path	Duration (weeks)
1-2-6-8-9	4+0+6+4=12
1-2-7-8-9	4+4+0+2=10
1-2-7-9	4+4+4=12
1-6-8-9	5+6+2=13
1-3-6-8-9	4+0+6+2=12
1-3-5-8-9	4+0+7+2=13
1-4-5-8-9	5+0+7+2=14
1-4-8-9	5+4+2=11

The critical path is 1-4-5-8-9, i.e., Δ-H-K.

Minimum project duration is 14 weeks
